



PICTORIAL PROGRESS OF (BSRP Ch: -0.675 to -0.050) OF CORRIDOR-2

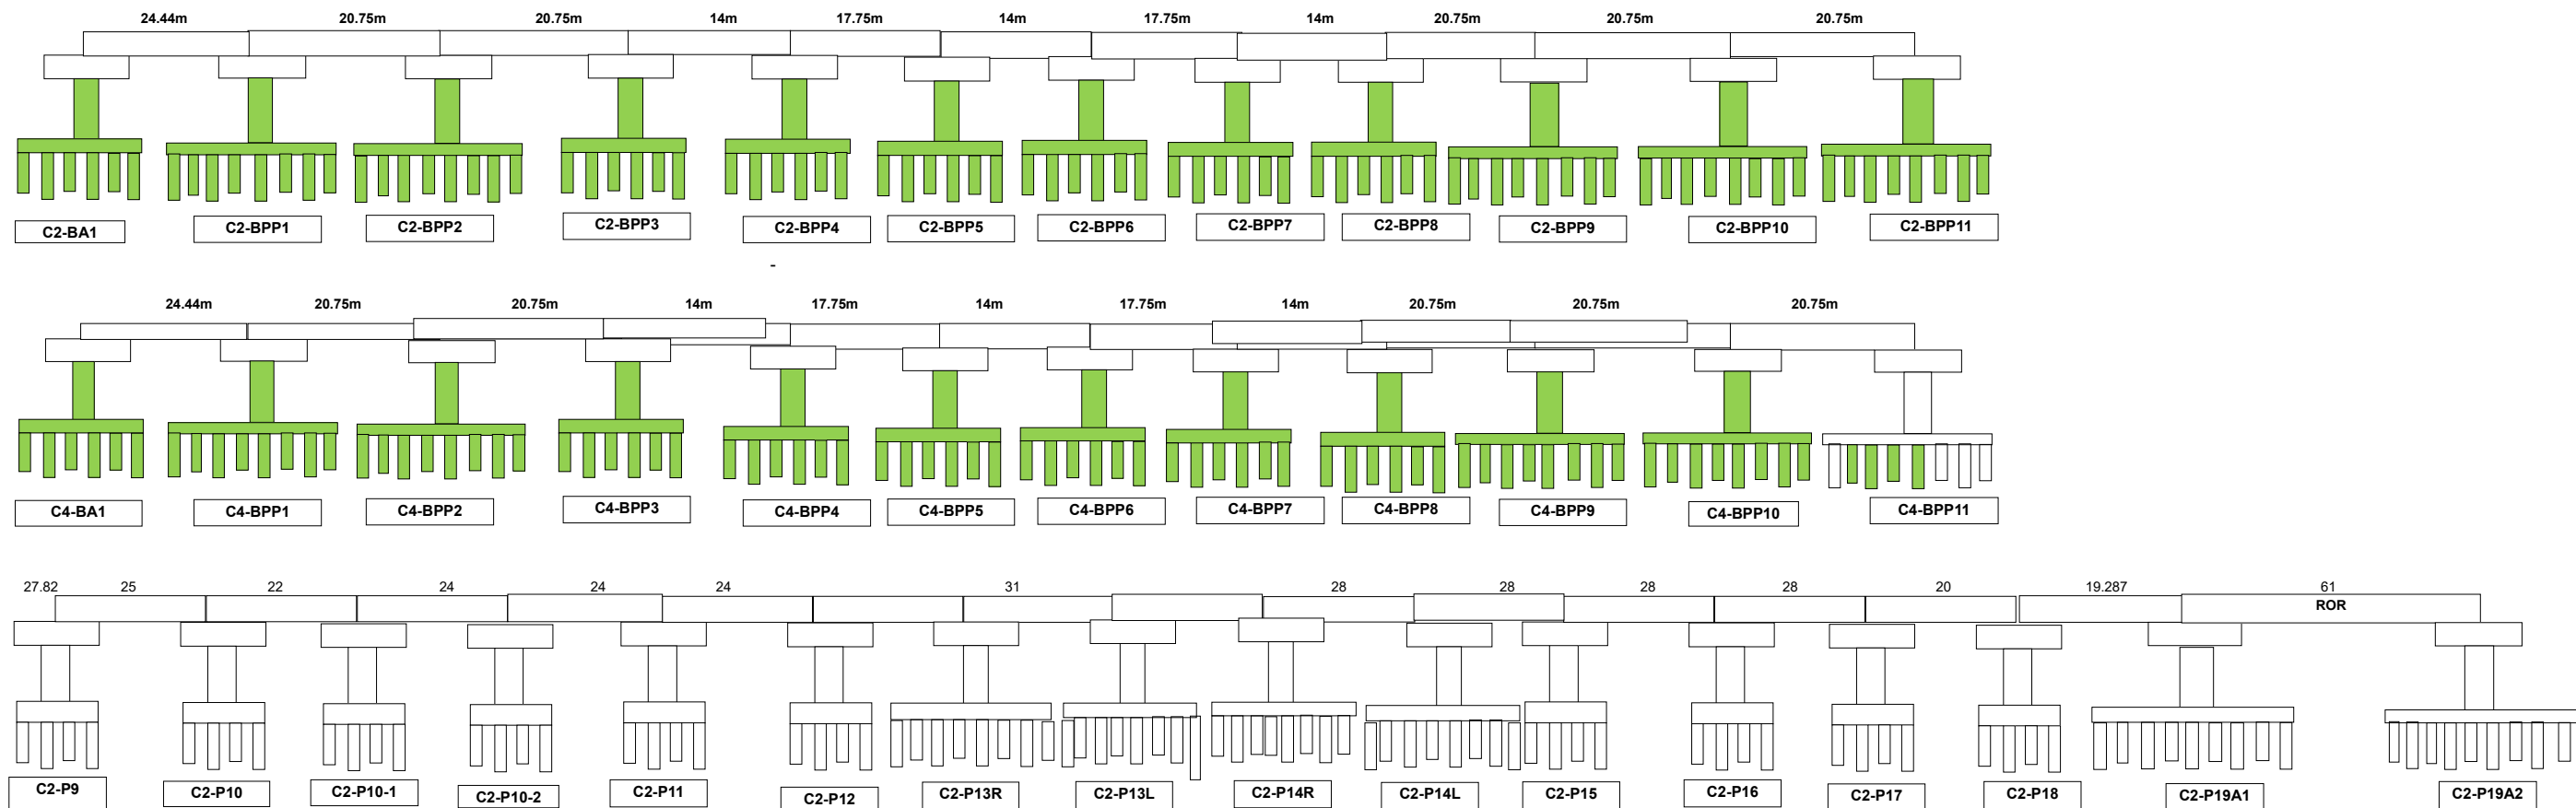

	Pile	Pile cap	Pier
Total scope	254 Nos	40 Nos	40 Nos
Completed	160 Nos	23 Nos	23 Nos
Balance	94 Nos	17 Nos	17 Nos

LEGEND	
	Work Completed


PICTORIAL PROGRESS OF (BSRP Ch: 11.230 to 16.755) OF CORRIDOR-2

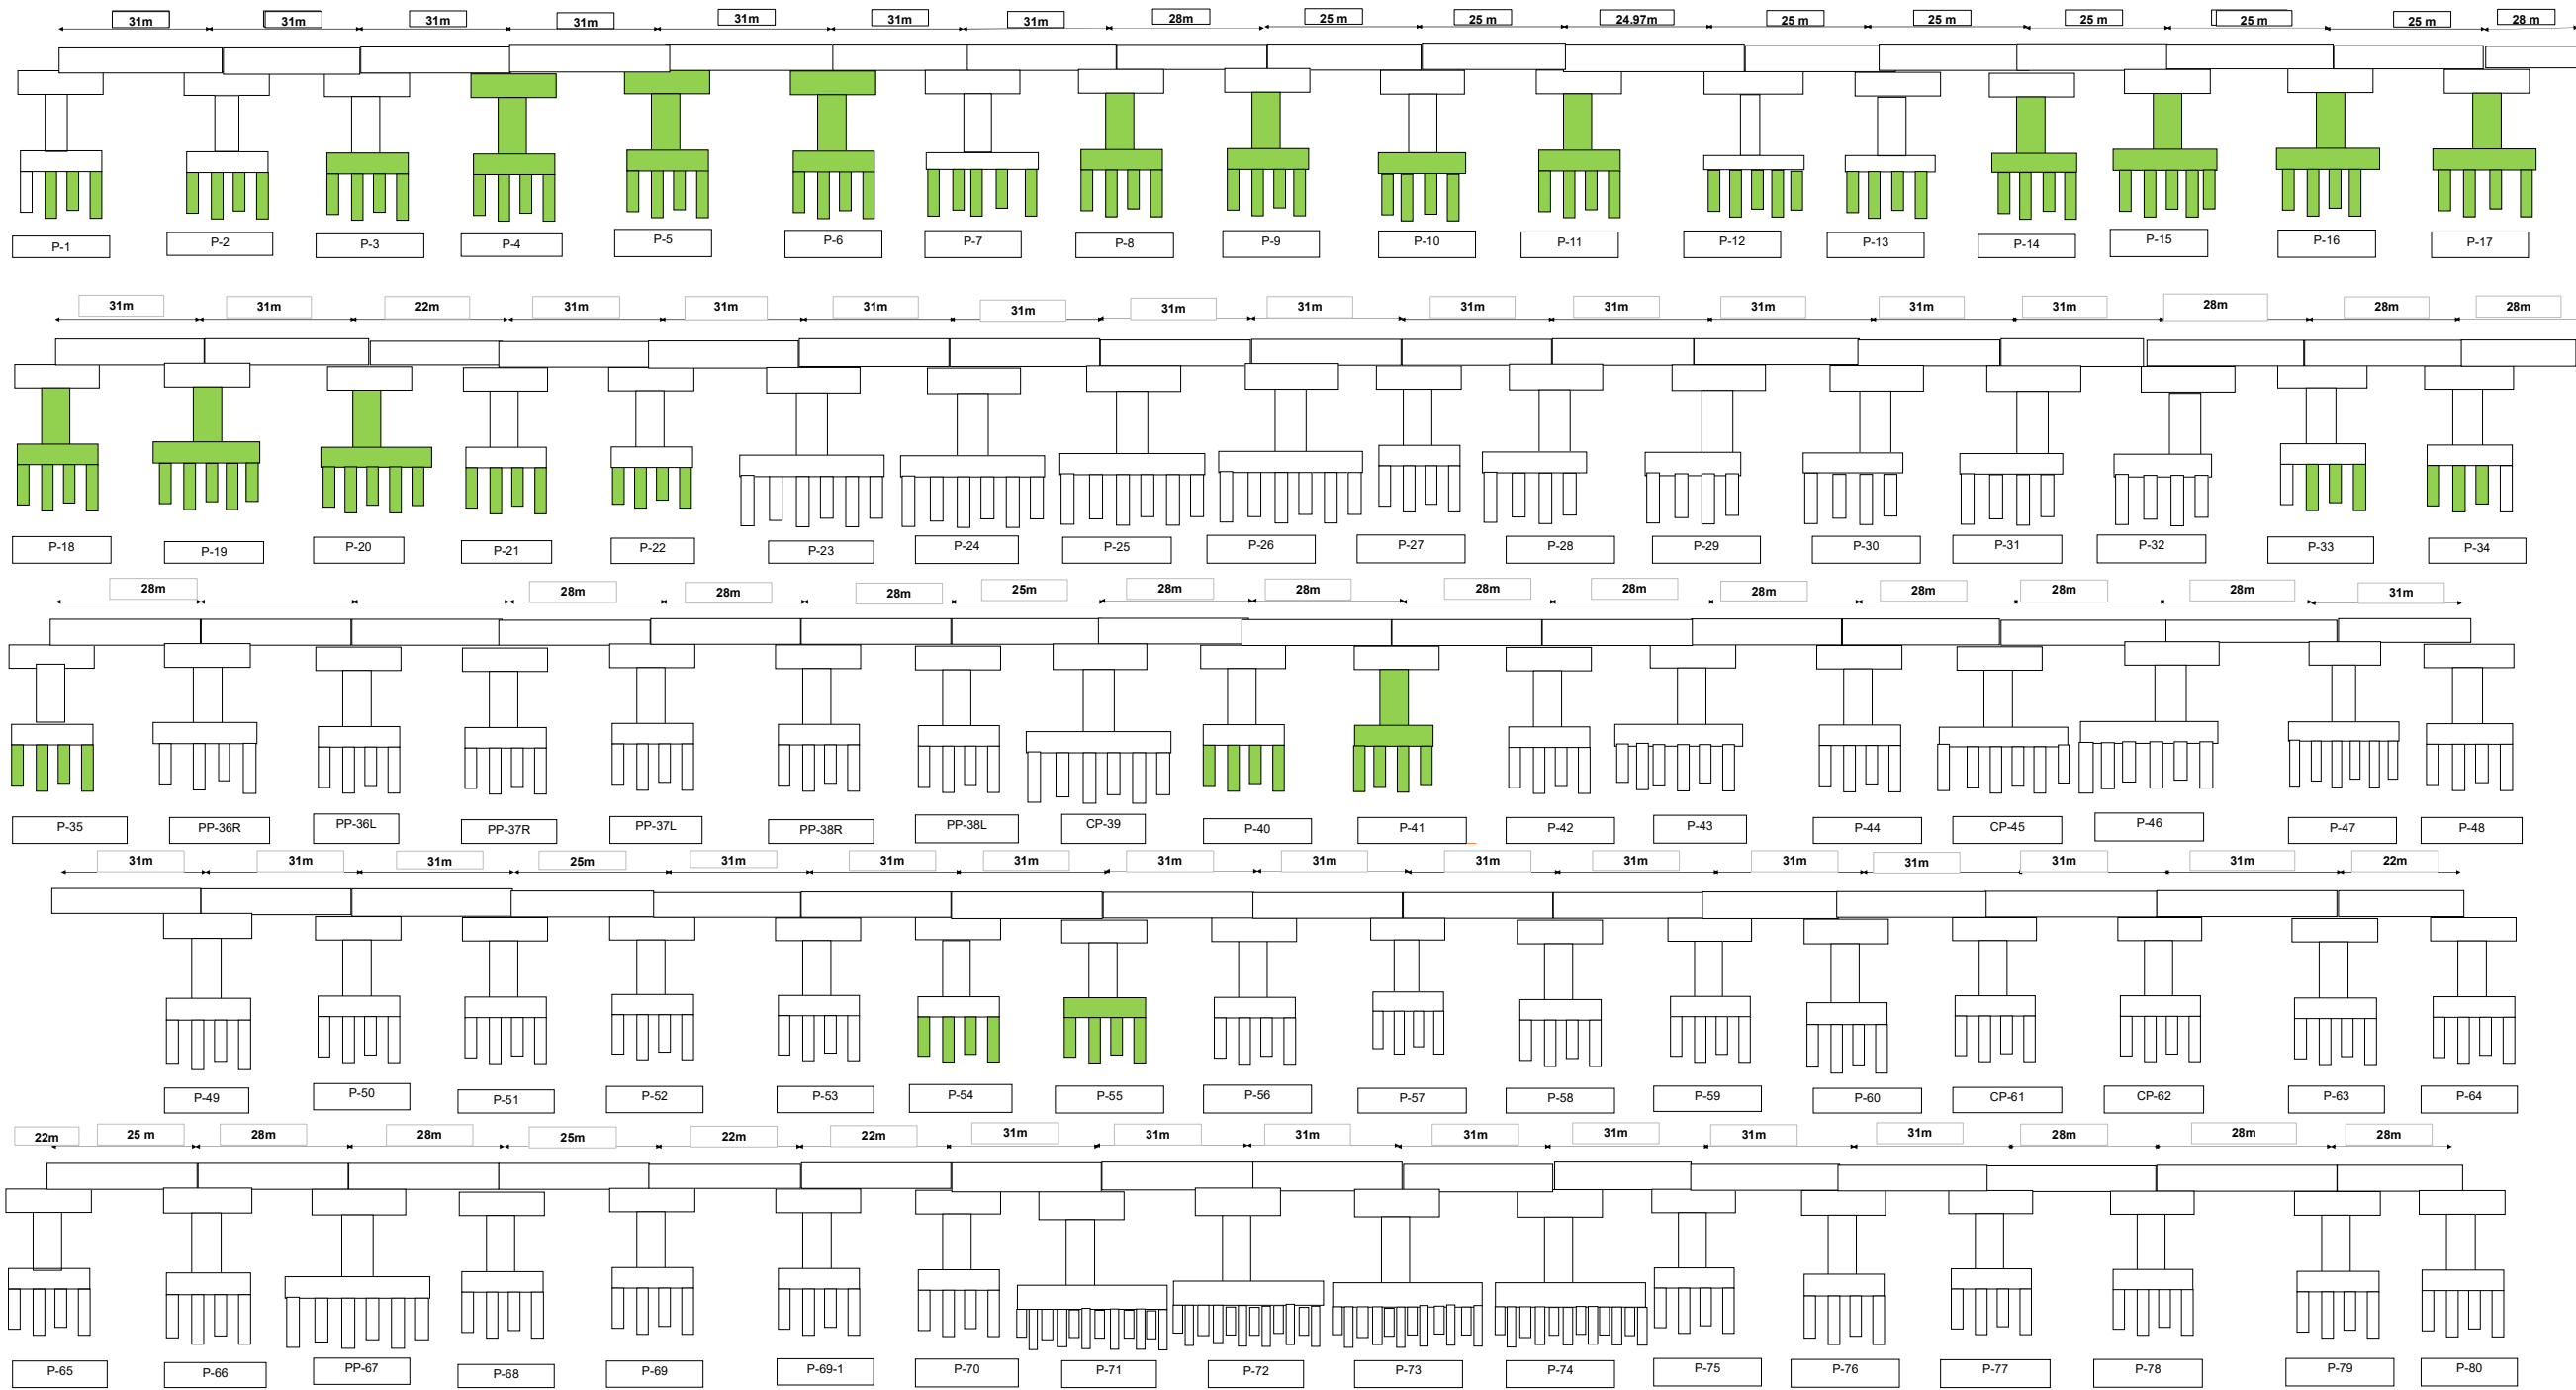

PICTORIAL PROGRESS OF (BSRP Ch: 11.230 to 16.755) OF CORRIDOR-2



PICTORIAL PROGRESS OF (BSRP Ch: 11.230 to 16.755) OF CORRIDOR-2

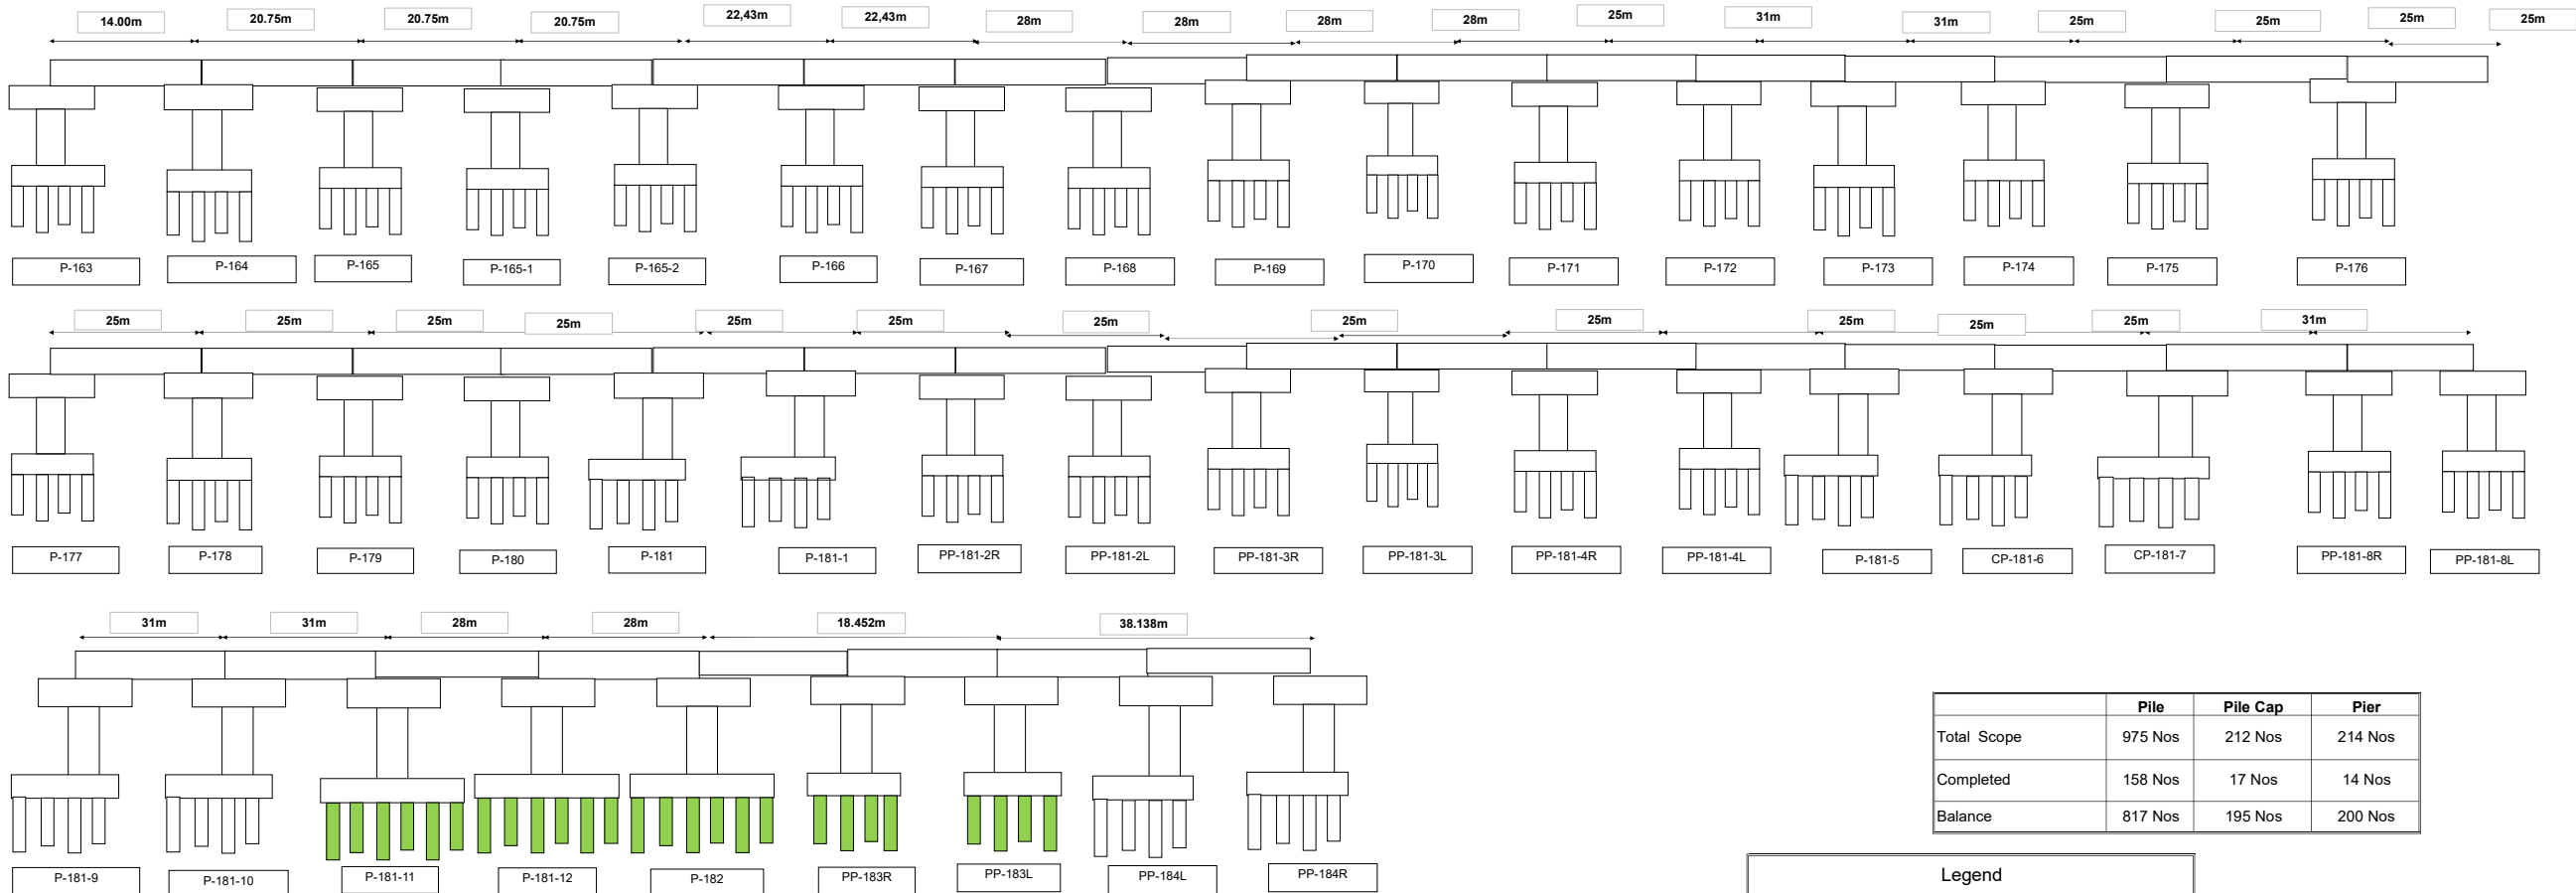

	Pile	Pile Cap	Pier
Total Scope	975 Nos	212 Nos	214 Nos
Completed	158 Nos	17 Nos	14 Nos
Balance	817 Nos	195 Nos	200 Nos

Legend	
	Work Completed

PICTORIAL PROGRESS OF (BSRP Ch: 16.755 to 18.400) OF CORRIDOR-2

